

Weekly Construction Progress Report #69

Period: 3/24/13 through 3/30/13

Project Work Performed:

- Continued interim construction survey staking to identify subgrade elevations.
- Continued compliance monitoring including air monitoring, weather monitoring, SWPPP monitoring and fugitive dust monitoring.
- Continued to collect field nuclear density testing to confirm compaction requirements.
- Completed taking delivery of Category I Landfill geosynthetics. Geosynthetics were stored within a covered building on the adjacent property.
- Completed preparing existing subgrade and completed initial site preparation activities within Stockpile #2 in preparation of the continuation of Category II backfill installation within the ConTop Basement.
- Continued the backfill activities within the southern end of the ConTop Basement with Category II material from within Stockpile #2.

Work Projected Next Week:

- Continue interim construction survey staking to identify subgrade elevations.
- Continue compliance monitoring including air monitoring, weather monitoring, SWPPP monitoring and fugitive dust monitoring.
- Continue to collect field nuclear density testing to confirm compaction requirements.
- Complete the backfill activities within the southern end of the ConTop Basement with Category II material from within Stockpile #2.

Former ASARCO Smelter Facility

Category 1 Landfill Construction

El Paso, TX



Current conditions within the PBA Channel and the Category 1 Landfill



Compaction of structural backfill within the ConTop Basement



Current conditions within the ConTop Basement

Weekly Construction Progress Report #69 (Continued)

Period: 3/24/13 through 3/31/13


Action Items/Safety:

- Loss Prevention System (LPS) tools
 - Loss Prevention Observation (LPO) – 2 (131)
 - Job Safety Analysis (JSAs) – 0 (10)
 - Near Loss – 0 (10)
 - Minor Equipment Damage – 1 (4)
 - Incidents – 0 (2)
 - Stop Work Authority 0 – (7)

Prepared by EJ Suardini, April 2, 2013



Loading of Category II materials from existing Stockpile #2

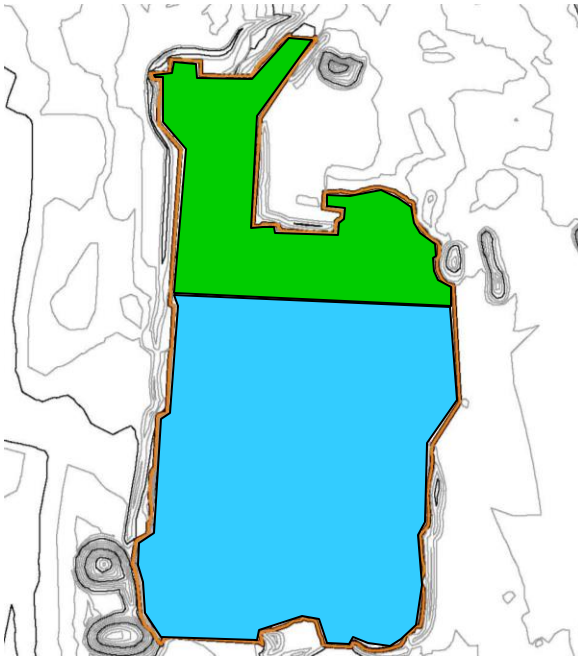

Progress Legend

Blue – Ongoing placement of structural fill

Green – Backfill Completed

Estimated Weekly Volume

	Estimated Quantity of CAT II Placement (Tons)	Estimated Quantity of East Borrow Excavation (Tons)	Estimated Quantity of ConTop Slag Pile Relocated (Tons)	Estimated Quantity of Structural Fill Material Installed PBA and CAT 1 (Tons)	Estimated Quantity of South Stack Berm Material (Tons)
Weekly Total	13,360	0	0	0	0
Total to Date	92,300	41,880	36,400	228,340	31,920
