

Weekly Construction Progress Report #37

Period: 7/29/12 through 8/4/12

Project Work Performed:

- Continued interim construction survey staking to identify subgrade elevations.
- Continued to screen and process clean onsite stockpile soils to meet structural fill material conformance specifications.
- Continued to load, transport, place, moisture condition and compact structural backfill within the Category 1 Landfill footprint to meet subgrade elevations.
- Continued compliance monitoring including air monitoring, weather monitoring, SWPPP monitoring and fugitive dust monitoring.

Work Projected Next Week:

- Continue interim construction survey staking to identify subgrade elevations.
- Continue to screen and process clean onsite stockpile soils to meet structural fill material conformance specifications.
- Continue to load, transport, place, moisture condition and compact structural backfill within the Category 1 Landfill footprint to meet subgrade elevations.
- Continue compliance monitoring including air monitoring, weather monitoring, SWPPP monitoring and fugitive dust monitoring.

Former ASARCO Smelter Facility

Category 1 Landfill Construction

El Paso, TX



Structural backfill placement and compaction within the Category 1 Landfill footprint



Material processing activities associated with mobile screen



Grading and compacting structural fill

Weekly Construction Progress Report #37 (Continued)


Period: 7/29/12 through 8/4/12

Action Items/Safety:

- Loss Prevention System (LPS) tools
 - Loss Prevention Observation (LPO) – 2 (68)
 - Job Safety Analysis (JSAs) – 0 (7)
 - Near Loss – 0 (5)
 - Minor Equipment Damage – 0 (3)
 - Incidents – 0 (2)
 - Stop Work Authority 0 – (7)



Prepared by EJ Suardini, August 8, 2012

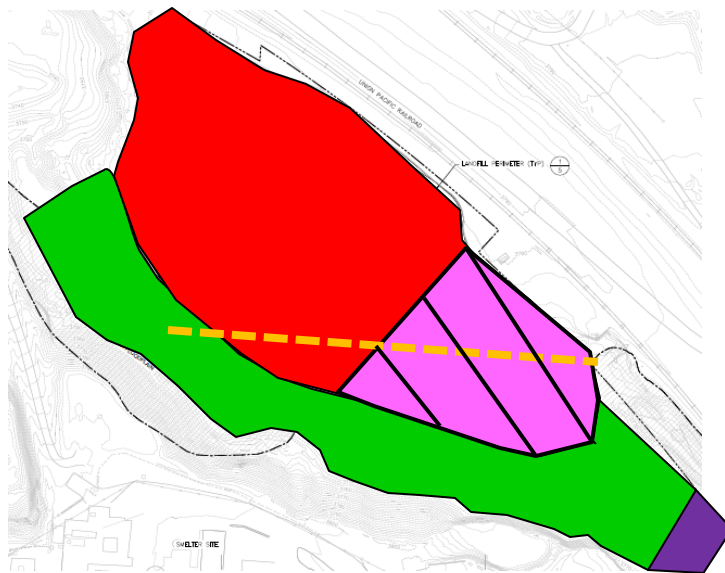

Placing, grading and moisture conditioning of structural fill

Progress Legend

**Blue – (Complete)
Excavation of Slag**

**Green – (Complete)
Excavation of Impacted soil
beneath Slag**

**Red – (Complete) Mass
Excavation Activity**

**Red (Hatch) – Current Work
Area**

**Orange – Removed
Sanitary/Storm Sewer Piping**

**Purple – Earthen Buttress
(Complete)**

Pink (Hatch) – Backfill Activities

Estimated Weekly Volume				
	Estimated Quantity of Slag Removed (Tons)	Estimated Quantity of Mass Excavation (Tons)*	Estimated Quantity of Structural Fill Material Installed (Tons)	Estimated Quantity of Subgrade Prepared (Tons)
Weekly Total	0	0	16,280	0
Total to Date	325,667	293,563	59,840	0

*Quantity includes the excavation of soil impacted material beneath slag.
