

Weekly Construction Progress Report #56

Period: 12/16/12 through 12/22/12

Project Work Performed:

- Continued interim construction survey staking to identify subgrade elevations.
- Continued compliance monitoring including air monitoring, weather monitoring, SWPPP monitoring and fugitive dust monitoring.
- Continued to screen and process CAT II soils to meet structural fill material conformance specifications associated with the CAT II Placement Plan.
- Completed the loading, hauling, placement, compaction and grading CAT II materials within the Ore Unloading Basement.
- Began basement preparation activities associated with the ConTop basement. Activities included the removal of protruding rebar, removal of miscellaneous loose debris and completion of basement floor penetrations.
- Continued to collect field nuclear density testing to confirm compaction requirements.

Work Projected Next Week:

- No scheduled field activities are scheduled from December 22nd through January 2nd in observance of the Holidays. Field activities are schedule to resume on January 3rd, 2013.



Screening of CAT II materials to meet 3-inch minus specifications



Subgrade preparation activities within the ConTop Basement



Removing existing rebar within ConTop Basement

Weekly Construction Progress Report #56 (Continued)

Period: 12/16/12 through 12/22/12


Action Items/Safety:

- Loss Prevention System (LPS) tools
 - Loss Prevention Observation (LPO) – 2 (106)
 - Job Safety Analysis (JSAs) – 0 (8)
 - Near Loss – 0 (7)
 - Minor Equipment Damage – 0 (3)
 - Incidents – 0 (2)
 - Stop Work Authority 0 – (7)

Prepared by EJ Suardini, December 27, 2012



Dust suppression along haul roads

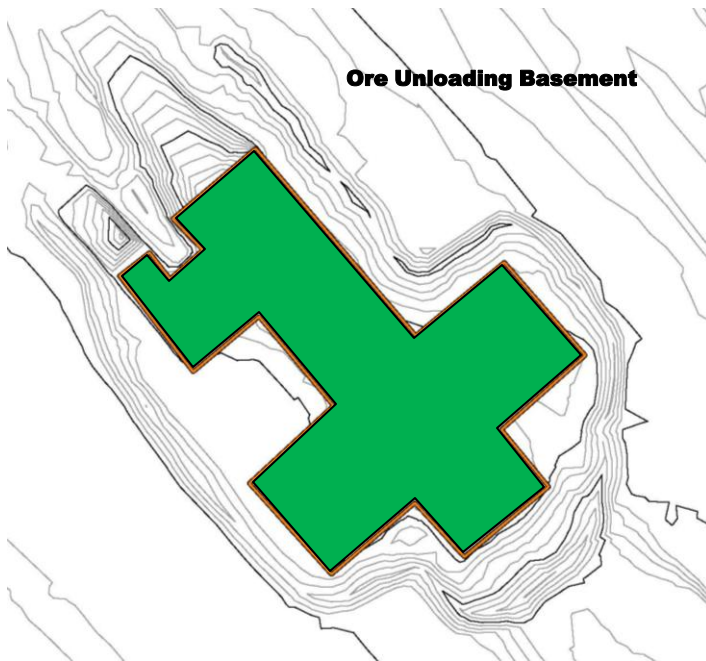

Progress Legend

Blue – Ongoing placement of structural fill

Green – Complete placement of structural fill

Estimated Weekly Volume

	Estimated Quantity of CAT II Placement (Tons)	Estimated Quantity of East Borrow Excavation	Estimated Quantity of Structural Fill Material Installed PBA and CAT 1 (Tons)	Estimated Quantity of Subgrade Prepared (Tons)
Weekly Total	5,270	0	0	0
Total to Date	29,640	293,563	186,860	0
